










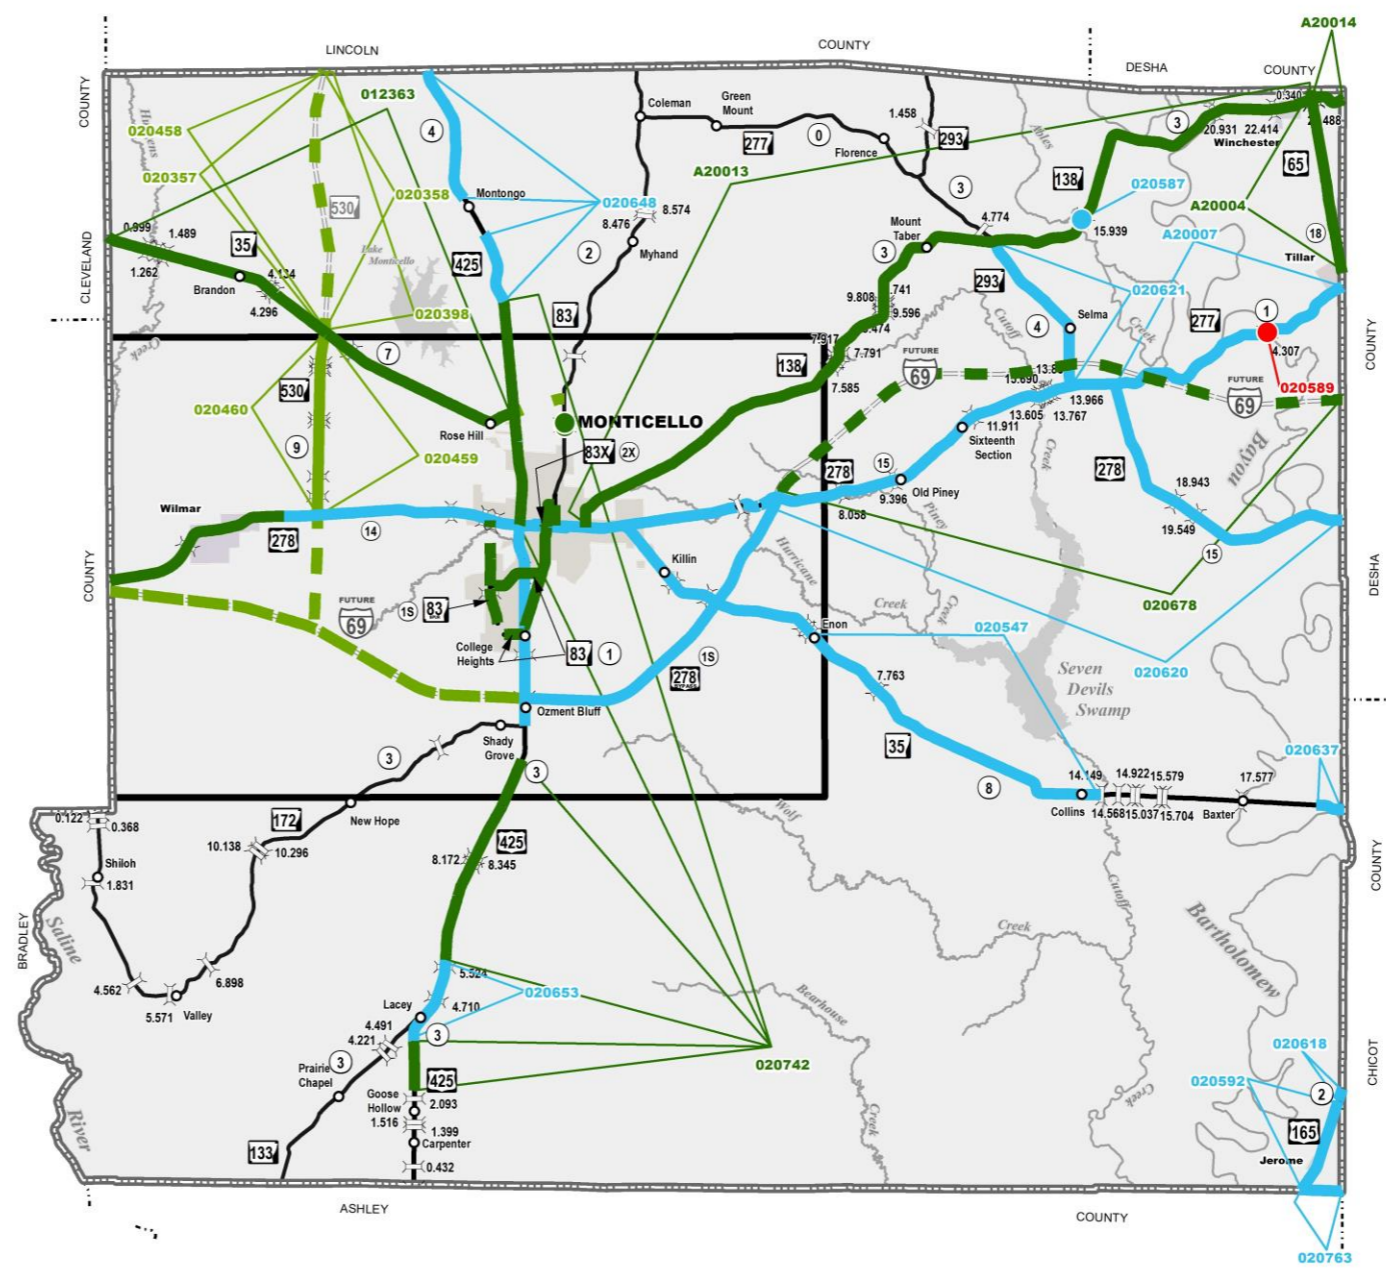


Status of Improvements

 Programmed	 Bridge
 Scheduled	 Interchange
 Under Construction	 Intersection Improvement
 Completed	 Slide Repair
	 Roadway
	 New Location




Drew County
District 2
Job Status Map

SUMMARY OF CONSTRUCTION PROJECTS

DREW COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
012062*	I-69 Connector Extension Study (F) Addt'l Rte.-Sec.: Ashley 530-10; Bradley 530-11; Union 530-12	530	9	Study	Completed	Aug. 2006	May. 2014	-	\$573,120	-	\$1,135,620
012363	Big Creek – Hwy. 425 (Sel. Secs.) (S) Addt'l Rte.-Sec.: Cleveland 35-5/6	35	7	Resurfacing	Scheduled	2023		11.13	\$3 - \$5 M	17.58	\$5 - \$10 M
012375*	Districts 1, 2 & 6 Bridge Preservation (2021) (S) Addt'l Rte.-Sec.: Lincoln 114-2; Phillips 20-1, 44-3; Saline 35-1	83	1	Bridge Rehabilitation	Under Construction	May. 2021	Mid 2022	0.04	\$831,771	0.20	\$4,158,856
020311	Hwy. 425 – Hwy. 83 Connection (Monticello) (S)	New		New Location	Programmed			1.20	\$1 - \$3 M	1.20	\$1 - \$3 M
020357	Hwys. 11/425 Connector – Hwy. 35 (Gr. & Strs.) (F) Addt'l Rte.-Sec.: Lincoln New	New		Grading & Structures	Programmed			6.32	\$15 - \$20 M	10.45	\$20 - \$30 M
020358	Hwys. 11/425 Connector – Hwy. 35 (Bs. & Surf.) (F) Addt'l Rte.-Sec.: Lincoln New	New		Base & Surfacing	Programmed			6.58	\$20 - \$30 M	11.07	\$30 - \$40 M
020365*	Hwys. 11/425 Connector – Hwy. 278 P.E. Addt'l Rte.-Sec.: Lincoln New	New		PE Only	Completed			-	\$0	-	\$6,734,428
020398	Hwys. 11/425 Connector – Hwy. 35 (Add'l. Lanes) (Gr. & Strs.) (F) Addt'l Rte.-Sec.: Lincoln New	New		Grading & Structures	Programmed			6.50	\$30 - \$40 M	10.50	\$50 - \$75 M
020458	Hwys. 11/425 Connector – Hwy. 35 (Add'l. Lanes) (Bs. & Surf.) (F) Addt'l Rte.-Sec.: Lincoln New	New		Base & Surfacing	Programmed			6.50	\$20 - \$30 M	10.50	\$30 - \$40 M
020459	Hwy. 35 – Hwy. 278 (Add'l. Lanes) (Gr. & Strs.) (F)	New		Grading & Structures	Programmed			4.50	\$20 - \$30 M	4.50	\$20 - \$30 M
020460	Hwy. 35 – Hwy. 278 (Add'l. Lanes) (Bs. & Surf.) (F)	New		Base & Surfacing	Programmed			4.50	\$10 - \$15 M	4.50	\$10 - \$15 M
020462*	Monticello Bypass P.E.	New		PE Only	Programmed			-	\$50 - \$75 M	-	\$50 - \$75 M
020470	Hwy. 278 West – Hwy. 425 (Gr. & MDS) (Monticello Bypass) (S)	New		Grading & Structures	Programmed			13.39	\$20 - \$30 M	13.39	\$20 - \$30 M
020471	Hwy. 425 – Hwy. 278 East (Gr. & Strs.) (Monticello Bypass) (F)	New		Grading & Structures	Completed	Sep. 2011	Oct. 2017	8.53	\$13,159,489	8.53	\$13,159,489
020475	Hwy. 83 Spur – Hwy. 278 Connector (Monticello) (F)	New		New Location	Scheduled	Jun. 2022		1.62	\$10 - \$15 M	1.62	\$10 - \$15 M
020480*	Southeast Arkansas Intermodal Facility (Ph. II) (Wilmar) (S)			Roadside Appurtenances	Programmed			-	< \$1 M	-	< \$1 M
020482	Hwy. 278 West – Hwy. 425 (Add'l Lanes) (Gr. & Strs.) (F)	New		Grading & Structures	Programmed			11.30	-	11.30	-
020483	Hwy. 278 West – Hwy. 425 (Add'l Lanes) (Bs. & Surf.) (F)	New		Base & Surfacing	Programmed			11.30	-	11.30	-
020484	Hwy. 425 – Hwy. 278 East (Bs. & Surf.) (Monticello Bypass) (S)	New		Base & Surfacing	Sub. Completed	Aug. 2017	Oct. 2018	8.63	\$16,197,356	8.63	\$16,197,356
020485	Hwy. 425 – Hwy. 278 East (Add'l Lanes) (Gr. & Strs.) (F)	New		Grading & Structures	Programmed			8.60	-	8.60	-
020486	Hwy. 425 – Hwy. 278 East (Add'l Lanes) (Bs. & Surf.) (F)	New		Base & Surfacing	Programmed			8.60	-	8.60	-
020518*	Southeast Arkansas Intermodal Facility (Ph. III) (Wilmar) (S)			Roadside Appurtenances	Under Construction	Aug. 2011		-	\$622,151	-	\$622,151
020519*	Southeast Arkansas Intermodal Facility (Ph. IV) (Wilmar) (S)			Roadside Appurtenances	Under Construction	Jul. 2013		-	\$560,411	-	\$560,411

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

DREW COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
020532*	Monticello City Square Sidewalks (ATEP-11) (S)			Enhancement	Completed	Mar. 2013	Sep. 2013	-	\$134,200	-	\$134,200
020547	Sandy Creek – Cutoff Creek (Overlay) (S)	35	8	Resurfacing	Completed	May. 2012	Aug. 2012	8.59	\$1,807,499	8.59	\$1,807,499
020552*	Hwy. 35 R.R. Surfacing (Monticello) (S)	35	0	RR Crossing	Completed	Mar. 2013	Apr. 2014	-	\$80,674	-	\$80,674
020557	Hwy. 278 – Sandy Creek (Overlay) (S)	35	8	Resurfacing	Completed	Jun. 2013	Sep. 2013	5.65	\$1,304,110	5.65	\$1,304,110
020560*	Monticello School District SRTS I (2012)			Roadside Appurtenances	Programmed			-	-	-	-
020564	Hwy. 425 (Monticello) (Sel. Sec.) (Overlay) (S) Addt'l Rte.-Sec.: Drew 425-4	425	3	Resurfacing	Completed	Apr. 2014	Aug. 2014	4.63	\$1,521,383	4.63	\$1,521,383
020587	Ables Creek Str. & Apprs. (S)	138	3	Structure & Approaches	Sub. Completed	Dec. 2018	Oct. 2020	0.34	\$3,204,170	0.34	\$3,204,170
020589	Bayou Bartholomew Str. & Apprs. (S)	277	1	Structure & Approaches	Under Construction	Jun. 2020	Late 2022	0.46	\$4,604,247	0.46	\$4,604,247
020592	Drew Co. Line – North & South (Mill & Inlay) (S) Addt'l Rte.-Sec.: Ashley 165-1	165	2	Resurfacing	Completed	Jun. 2016	Oct. 2016	2.40	\$475,540	9.34	\$1,850,643
020611	Hwy. 278 West – Hwy. 425 (Major Strs. & Surf.) (Monticello Bypass) (S)	New		Base & Surfacing	Programmed			13.39	\$15 - \$20 M	13.39	\$15 - \$20 M
020618	South of Drew Co. Line – Hwy. 35 (Sel. Secs.) (S) Addt'l Rte.-Sec.: Chicot 165-3	165	2	Bridge Rehabilitation Resurfacing	Completed	Feb. 2018	Nov. 2018	0.13	\$30,627	5.76	\$1,357,033
020620	Monticello – McGehee (Sel. Secs.) (S) Addt'l Rte.-Sec.: Desha 278-16	278	15	Resurfacing	Completed	Jan. 2018	Jul. 2018	20.22	\$3,891,398	24.92	\$4,795,927
020621	Hwy. 138 – Hwy. 278 (S)	293	4	Resurfacing	Completed	May. 2018	Oct. 2018	4.27	\$1,355,760	4.27	\$1,355,760
020635	Hwy. 172 – Old Warren Rd. (Monticello) (S)	425	3	Resurfacing	Completed	Jan. 2017	Jul. 2017	4.03	\$2,208,708	4.03	\$2,208,708
020637	West of Drew Co. Line – Hwy. 65 (S) Addt'l Rte.-Sec.: Chicot 35-9	35	8	Resurfacing	Completed	Apr. 2017	Oct. 2017	0.71	\$205,554	5.33	\$1,543,104
020648	Monticello – Star City (Sel. Secs.) (S) Addt'l Rte.-Sec.: Lincoln 425-5	425	4	Resurfacing	Sub. Completed	Feb. 2020	Sep. 2020	5.13	\$1,811,638	9.33	\$3,294,851
020653	Co. Rd. 28 – South (S)	425	3	Resurfacing	Sub. Completed	Feb. 2020	Oct. 2020	2.15	\$714,297	2.15	\$714,297
020669*	Lake Monticello Trail (TAP-16) (S)			Roadside Appurtenances	Programmed			-	< \$1 M	-	< \$1 M
020678	Hwy. 278 – Hwy. 65 (S) Addt'l Rte.-Sec.: Desha New	New		New Location	Scheduled	Apr. 2022		15.15	\$50 - \$75 M	16.97	\$75 - \$100 M
020719*	Monticello Hwys. 278 & 425 Sidewalks (TAP-19) (S) Addt'l Rte.-Sec.: Drew 425-3/4	278	14	Enhancement	Programmed			-	< \$1 M	-	< \$1 M

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

DREW COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date		County Totals		Project Totals	
							Date	Date	Length (Mi)	Cost	Length (Mi)	Cost
020722	Hwy. 83 Resurfacing (Sel. Secs.) (Monticello) (S) Addt'l Rte.-Sec.: Drew 83-1S/2/2X, CS	83	1	Resurfacing	Scheduled	2023			6.43	\$1 - \$3 M	6.43	\$1 - \$3 M
020726*	Hwy. 138 RR Signals (Winchester) (S)	138	3	Safety Improvements	Programmed				-	< \$1 M	-	< \$1 M
020727*	District 2 Sealing Program (2020) (S) Addt'l Rte.-Sec.: Various	144	1	Sealing	Programmed				11.90	< \$1 M	81.83	\$1 - \$3 M
020741	Bradley Co. Line – Wilmar (S)	278	14	Resurfacing	Scheduled	2024			4.80	\$3 - \$5 M	4.80	\$3 - \$5 M
020742	Ashley Co. Line – Monticello (Sel. Secs.) (S) Addt'l Rte.-Sec.: Drew 425-4	425	3	Resurfacing	Scheduled	2024			11.99	\$5 - \$10 M	11.99	\$5 - \$10 M
020763	Jerome – McMillan Corner (S) Addt'l Rte.-Sec.: Chicot 144-2	144	1	Resurfacing	Sub. Completed	May. 2021	Oct. 2021	0.99	\$411,146		9.27	\$3,849,823
020765*	Monticello County Library Sidewalks (TAP-20) (S)			Enhancement	Programmed				-	< \$1 M	-	< \$1 M
020767*	Lake Monticello Trail Ph. 1 (Monticello) (RTP-20) (S)			Enhancement	Programmed				-	< \$1 M	-	< \$1 M
020775	Hwy. 83 Strs. & Apprs. (S)	83	2	Structures and Approaches	Scheduled	Nov. 2023			-	\$1 - \$3 M	-	\$1 - \$3 M
A20002	Wilmar – Monticello (S) Addt'l Rte.-Sec.: Drew 278-15/15X	278	14	Resurfacing	Sub. Completed	Apr. 2020	Oct. 2020	9.32	\$4,883,547		9.32	\$4,883,547
A20004	Winchester – Chicot Co. Line (Sel. Secs.) (S) Addt'l Rte.-Sec.: Desha 65-18/19	65	19	Resurfacing	Scheduled	Apr. 2022			6.24	\$1 - \$3 M	12.97	\$3 - \$5 M
A20007	Hwy. 278 – Hwy. 65 (S) Addt'l Rte.-Sec.: Desha 277-1	277	1	Resurfacing	Sub. Completed	Feb. 2021	Sep. 2021	6.09	\$1,658,361		6.22	\$1,693,761
A20010*	District 2 Resurfacing Program (2021) (S) Addt'l Rte.-Sec.: Various	35	8	Resurfacing	Programmed				20.26	< \$1 M	75.48	< \$1 M
A20013	Monticello – Hwy. 65 (S)	138	3	Resurfacing	Scheduled	Apr. 2022			23.39	\$3 - \$5 M	23.39	\$3 - \$5 M
A20014	Hwy. 65 – Hwy. 1 (S) Addt'l Rte.-Sec.: Desha 138-4	138	3	Resurfacing	Scheduled	Jan. 2022			0.82	< \$1 M	13.69	\$1 - \$3 M
A20015*	District 2 Resurfacing Program (2022) (S) Addt'l Rte.-Sec.: Various	293	3	Resurfacing	Programmed				5.18	< \$1 M	47.54	\$1 - \$3 M
C22001*	Wilmar Street Improvements (Sel. Secs.) (S)	CS		Resurfacing	Completed	Apr. 2014	Jul. 2014	1.53	\$255,339		1.53	\$255,339
C22002*	Wilmar Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jun. 2018	Aug. 2018	2.14	\$313,330		2.14	\$313,330
C22003*	Winchester Overlay (Sel. Secs.) (S)	CS		Resurfacing	Sub. Completed	Jan. 2020	May. 2020	0.81	\$199,312		0.81	\$199,312
C22004*	Monticello Overlay (S)	CS		Resurfacing	Sub. Completed	May. 2020	Nov. 2020	1.36	\$264,851		1.36	\$264,851

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

DREW COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or Sub. Comp. Date</i>	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
C76006*	Monticello & Star City Overlay (Sel Secs) (S) Addt'l Rte.-Sec.: Lincoln CS	CS		Resurfacing	Completed	Jan. 2014	Mar. 2014	1.45	\$201,768	3.25	\$448,372
C76044*	Arkansas City, Dermott & Tillar Overlay (S)	CS		Resurfacing	Completed	Feb. 2019	May. 2019	1.16	\$31,875	4.55	\$798,399
R20089*	Pine Bluff – Mississippi Line P.E. Addt'l Rte.-Sec.: Various	65	18	PE Only	Programmed			-	-	-	-
R20107*	La. Line – Pine Bluff P.E. Addt'l Rte.-Sec.: Various	425	3	PE Only	Programmed			-	-	-	-
SA2244*	Hwy. 425-East (Overlay) (S)	CR		Resurfacing	Completed	May. 2012	Jun. 2012	2.50	\$381,558	2.50	\$381,558
SA2245*	Drew County Overlay (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jun. 2014	Oct. 2014	8.36	\$1,126,760	8.36	\$1,126,760
SA2246*	Drew County Overlay No. 2 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Aug. 2016	Oct. 2016	3.88	\$553,191	3.88	\$553,191
SA2247*	Co. Rd. 92 - Co. Rd. 99 (Overlay) (S)	CR		Resurfacing	Completed	Jul. 2018	Dec. 2018	3.45	\$439,958	3.45	\$439,958
Totals For All Projects In Drew County								200.52	\$173,906,579		

* Job not shown on county map.
